

## TOURISM INFRASTRUCTURE AND ENTERPRISE ZONE AUTHORITY

6th & 7th Floors, Tower 1
Double Dragon Plaza
Double Dragon Meridian Park
Macapagal Avenue corner
Edsa Extension Bay Area
Pasay City 1302

**)** (+

(+632) 249-5900 loc.701



ocoo.tieza.gov.ph



www.tieza.gov.ph

November 23, 2020

## **CERTIFICATE OF 100% COMPLETION**

This is to certify that the RESTORATION & REHABILITATION of BANAUE RICE TERRACES Project located at Banaue, Ifugao Province undertaken by HAUSLAND Construction is 100% complete on October 22, 2020.

The work was satisfactorily done in accordance with the approved plans and specifications.

Certified by:

JOSELITO J. AURE

**Project Engineer** 

Noted:

RESURRECION L'ASPURIA

Manager

**Construction Management Department** 

Concurred:

**NESTOR M. DOMALANTA**Asst. Chief Operating Officer

Architectural & Engineering Services Sector





## **TOURISM** INFRASTRUCTURE AND **ENTERPRISE** ZONE AUTHORITY

6th & 7th Floors, Tower 1 Double Dragon Plaza Double Dragon Meridian Park Macapagal Avenue corner Edsa Extension Bay Area Pasay City 1302

(+632) 8249-5900 loc.746

ocoo@tieza.gov.ph

www.tieza.gov.ph

**MEMORANDUM** 

**FOR** 

: The Assistant Chief Operating Officer

Architectural and Engineering Services Sector

THRU

: The Manager

Construction Management Department ( )

SUBJECT

: Inspection Report No. 10, as per T.O.no. 2020-11-0460

dated November 17, 2020

DATE

: November 23, 2020

A. PROJECT BRIEF:

NAME of PROJECT

: RESTORATION & REHABILITATION OF

**BANAUE RICE TERRACES** 

LOCATION

: Banaue, Ifugao

: By contract

: PhP58,558,236.06

: HAUSLAND Construction

**PROPONENT** 

LGU Province of Ifugao, Represented by

Governor JERRY U. DALIPOG

MODE OF IMPLEMENTATION

**CONTRACT AMOUNT** 

CONTRACTOR

PROJECT DURATION

**DATE START** 

COMPLETION DATE

SUSPENDED SINCE (ECQ)

**RESUMED ON** 

: 180 C.D. : January 14, 2020 : July 11, 2020

: March 18, 2020 : July 6, 2020

**VARIATION ORDER no.1** 

AMOUNT / DURATION

: PhP0.00 / Zero (0) C.D.

**REVISED COMPLETION DATE** 

: October 22, 2020

B. SCOPE OF WORK: (V.O. no.1 INCLUDED)		AMOUNT, Php	Wt.,%	Prev.,%	This Period,%	To Date,%
I. General Requirements						
a. Temporary Facilities		94,073.04	0.161	0.161	0.000	0.161
b. Project Signage		20,727.00	0.035	0.035	0.000	0.035
c. Safety & Health Program		161,840.80	0.276	0.276	0.000	0.276
II. Stone Walling			S Marin			
a. Clearing Works		158,003.60	0.270	0.270	0.000	0.270
b. Excavation Works		381,237.48	0.651	0.651	0.000	0.651
c. Riprapping Works	EN RELIGION SHE	54,422,434.14	92.937	92.937	0.000	92.937
III. Other Matters/Special Provision	ins		(C. 1752)			
a. Tramlines		3,319,920.00	5.669	0.000	5.669	5.669
	OTAL	58,558,236.06	100.000	94.331	5.669	100.000

Actual Project Accomplishment: 100.00% as of October 22, 2020

C. FINDINGS/REMARKS:

1. Final technical site inspection and pictorial were conducted on November





## TOURISM INFRASTRUCTURE AND ENTERPRISE ZONE AUTHORITY

6th & 7th Floors, Tower 1
Double Dragon Plaza
Double Dragon Meridian Park
Macapagal Avenue corner
Edsa Extension Bay Area
Pasay City 1302

(+632) 8249-5900 loc.746
cocoo@tieza.gov.ph
www.tieza.gov.ph

- Punch listing of defects was performed by the undersigned on October 13, 2020 as per letter request of the Contractor dated September 8, 2020 requesting to conduct Punch Listing inspection & found out to be fully rectified/corrected during this inspection.
- 3. All Stone Walling in Bgy. Bangaan & Bgy. Batad were evaluated to be 100% completed.
- 4. List of the more than 500 restored & rehabilitated stone walls of the terraces (Volume of Riprapping in Cubic Meters) located in Bgy. Bangaan & Bgy. Batad were already validated, verified, & recorded & being completed for final submission.
- 5. The project is 100% complete & all set for Tieza's CPES-IU Team to conduct their Final Evaluation.


For your information, Sir.

JOSELITO L. AURE Project Engineer

Attachments:

Project Pictorial
Tramlines Pictorial



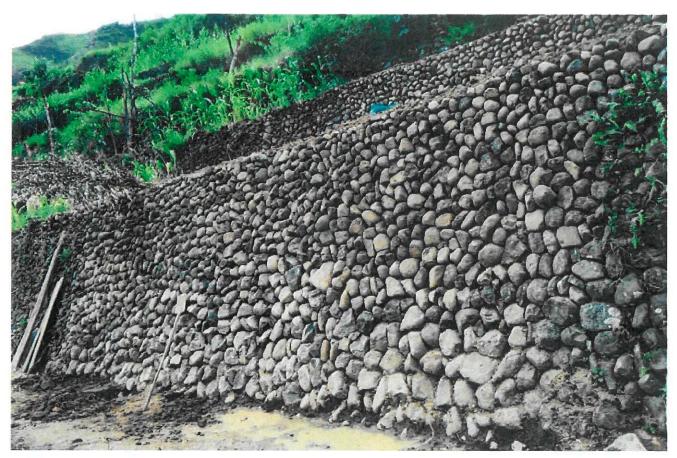



RESTORATION & REHABILITATION of BANAUE RICE TERRACES Project "FINAL INSPECTION"
Bgy. Bangaan & Bgy. Batad, Banaue, Ifugao Province
Pictorial – November 19-20, 2020
